

Airport Rehabilitation Project News Bulletin No. 2

Construction has commenced and it is time for another project update.

CONSTRUCTION SCHEDULE:

Tristar Electrical and subcontractors have arrived and been busy working on-site for the past week; initially during the day and now during the night. NOTAMS (Notice to Airman) have been issued which mirror this chart:

	Bravo	Charlie	Runway
(current condition) to Friday Jul 29 th @ 7am	Closed	Open	Night closures - weekdays
Friday Jul 29 th @ 7am to Monday Aug 1 st @ 7pm	Open	Open	Open
Monday Aug 1 st @ 7pm to Thursday Aug 4 th @ 7am	Open	Closed	Night closures - weekdays
Thursday Aug 4 th @ 7pm to Tuesday Aug 9 th @ 7am	Closed	Open	Night closures - weekdays
Tuesday Aug 9 th @ 7am to Friday Aug 12 th @ 7pm	Closed	Open	Open


NOTE: This schedule is subject to change without advanced notice; however, the contractor and airport will make every effort to maintain these commitments.

CONSTRUCTION UPDATE:

- ◆ A complete survey of the project area on the airfield has been completed
- ◆ Layout, excavation, installation of rebar and conduits of five (5) new duct banks including concrete pour has been completed
- ◆ Milling of perforated PVC subdrain crossing Taxiway Bravo
- ◆ Excavation of manholes



New PVC perforated drain pipe.

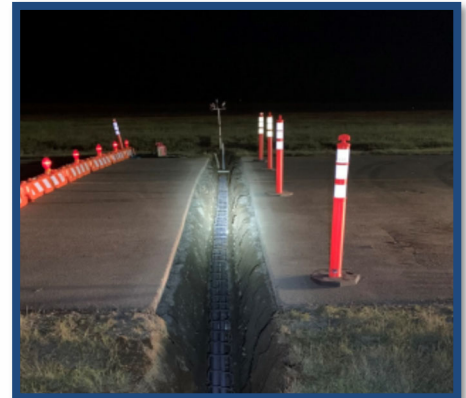

As seen in this night shift photo, rebar and new conduits installed across Taxiway Bravo prior to concrete pour.

Learn more at: campbellriver.ca/construction.

Questions? Email the Project Team at: airport.reception@campbellriver.ca or contact us directly at 250-923-5012.

